

NrollXpert: Simple Application, Seamless Enrolment	2
Team capacity for project	3
Meeting Schedule & Minutes	4
Project Objectives and Scope	10
Project Charter	12
Project Plan	14
Product Backlog	17
Milestone Plan	27
Client Communication plan	32
SharePoint Site for the Documentation	34
Risk Register :	35
Test Strategy and Summary	36
Test Plan	37
1. Test Plan and Scheduling	38
2. Test Scope	40
3. Testing Objective	42
4. Done (DoD)	44
5. Testing Strategy	45
6. Test Execution Strategy	49
Test Summary Report	53
1. Test Summary Report Sprint 1	54
2. Test Summary Report Sprint 2	55
3. Test Summary Report Sprint 3	56
4. Test Summary Report Sprint 4	57
Testing Sign-Off	58
Lesson Learned :	61
Definition Of Done Checklist	62

App for continuous feedback in enrolment process

NrollXpert: Simple Application, Seamless Enrolment

Blog Posts

 [NrollXpert: App for continuous feedback in the enrolment process:](#) created by [Snigdha Nath](#) Nov 15, 2023
[A well-serviced application & enrolment app](#)

Team capacity for project

Name	Role
Areeba	Product Owner
Snigdha	Scrum Master
Ahmed Hobeishy	Developer
Silpa Prasad Sivaprasad	Developer
Mustafa Ali	Developer
Farhana	Developer
Muhammad Tallal Bin Shahid	Developer
Anjali Khanduri	Tester
Nitika Deswal	Tester
Lakshay Saini	Business Analyst



Meeting Schedule & Minutes

Date	Attendees	Agenda	Notes, decisions and action items
Meeting 01-16/11/2023	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath @Farhana Binta Shaheed)	Discussion about roles, App requirement by client, Scope of the App.	Roles were assigned to each member, discussion about the pitch video had been done. Scope of the App were decided. Milestones plan was assigned to @Areeba Ilyas Video compilation was assigned to @Mustafa Ali (BJ) Initial Requirement plan was assigned to business analyst and developer @Ahmed Hobeishy and @LAKSHAY SAINI
Meeting 02-20/11/2023	Team C (@Areeba Ilyas @Ahmed Hobeishy	• Client response • BA requirements (ongoing) • Scopes Discussions	Software requirements were discussed with the teams. All the IT tools spaces were introduced to teams for project

	@Anjali Khanduri @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath @Farhana Binta Shaheed)	• Software Requirement Specification Documents	Discussion on the Client response with all teams Assigned SRS document to @Ahmed Hobeishy Confluence managements to @Areeba Ilyas and @LAKSHAY SAINI Jira Managements to @Snigdha Nath and @Ahmed Hobeishy
Meeting 03-30/11/2023	@Muhammad Tallal Bin Shahid @Snigdha Nath @LAKSHAY SAINI @Ahmed Hobeishy @Areeba Ilyas	• Scope Finalization + Backlog creation • BA requirements (revised) • Roles and Responsibilities	Discussed revised software requirement specification plan. Discussion about the user stories and epics. Increased members in the Developers team Reminders for next submission to the developers team.

Meeting 04- 28/12/2 023	@Muh amma d Tallal Bin Shahi d @Are eba Ilyas @Farh ana Binta Shahe ed @Ah med Hobeis hy @Silp a Prasad Sivapr asad @Snig dha Nath @LAK SHAY SAINI @Anja li Khand uri @Nitik a	• Progress (Scrum practice) • Development update	Discussion with the developers related to screens of the applications. Assign task to the Jira team for updating of sprints.
----------------------------------	--	--	--

	Deswa I		
Meeting 05- 02/01/2 024	@Ah med Hobeis hy @Are eba Ilyas @Snigdha Nath @Mustafa Ali (BJ) @Farhana Binta Shaheed @Silpa Prasad Sivaprasad @Muhammed Tallal Bin Shahid @LAKSHAY SAINI	• Progress (Scrum practice) • Test plan	Discussion related to test plans was done. Developers shown progress individually. Discussion related to presentation was done. Assigned Presentation slides to @Snigdha Nath and @LAKSHAY SAINI

Meeting 06-05/01/2024	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @Farhana Binta Shaheed @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath)	• Progress + Further plan • Discussion technical issues (Test) • Further plan	Discussed issues related to testing and presentations. Discussed all the things related to Trello.
Meeting 07-08/01/2024	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @Farhana Binta Shaheed @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ)	• Discussion on the Release date and plan and DATE	Divided all stuff related to presentations and final touches to the confluence.

	@Nitika Deswal @Silpa Prasad Sivaprasa d @Snigdha Nath)		
Meeting 08- 11/01/20 24	<u>Team</u> C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @Farhana Binta Shaheed @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasa d @Snigdha Nath)	• Final Presentation Revision	All the changes made to the Slides and presentation scripts.

Project Objectives and Scope

Purpose and Objective:

Purpose:

The project aims to enhance the application and enrolment process for the different programs by replacing the current email-based system with a comprehensive web application.

Objective:

1. Create a user-friendly experience for applicants.
2. Make it easier for university staff to manage all applications.
3. Digitize the Enrollment process.

Users:

1. Applicants

- Create accounts.
- submit required documents.
- track progress

2. University Staff

- Access applicant information,
- Manage every application (review documents, provide feedback, update statuses...)

Features:

1. User Authentication

- Secure login for applicants and university staff.

2. profiles for applicants and staff.

3. Dashboard:

- Show an overview of the application process and the status of the application.

4. Step-by-step guidance through the enrollment process.

- Checklist for required documents.

- Secure file upload for required documents.
- Notifications for completed steps and pending actions.
- 5. In-app messaging for communication between applicants and university staff.
- 6. Support and Guidance:
 - FAQs and resources for common queries.

Proposed Technology Stack:

Frontend: Angular

Backend: [ASP.NET Core, an open-source web development framework | .NET](#)

Database: PostgreSQL

Hosting: AWS or Heroku for application hosting.

Example of current Enrollment management systems to study and develop the best possible product:

- [The MIT Executive MBA | MIT Executive MBA | MIT Sloan](#)
- <https://admission.stanford.edu/apply/>
- [How to Apply](#)

Project Charter

1. Project Overview:

The Continuous Feedback Application for Enrollment project aims to implement a user-friendly and effective application that facilitates easy application and enrollment process. The application will enhance communication, identify areas for improvement, and contribute to the overall optimization of the enrollment experience for all stakeholders.

2. Project Objectives:

- Develop a web application for better application and the enrollment process.
- Implement a user-friendly interface accessible to students and administrators.
- Promote transparency and collaboration among stakeholders.

3. Scope:

The project will encompass the following:

- Design and development of the web Application.
- Integration with existing enrollment systems.
- Testing and quality assurance to guarantee the application's functionality.
- Deployment of the application to production servers.

4. Stakeholders:

- **Product Owner:** @Areeba Ilyas
- **IT Department:** @Ahmed Hobeishy @Mustafa Ali (BJ) @Muhammad Tallal Bin Shahid @Silpa Prasad Sivaprasad @Farhana Binta Shaheed
- **End-users:** FH Students / willing to join FH
- **Administrators:** FH Faculty

5. Deliverables:

- Fully functional Application.
- User documentation and training materials.
- Integration with existing enrollment systems.

6. Timeline:

The project is scheduled to start on 27-10-2023 and is expected to be completed by 12-01-2024. The timeline may be adjusted based on project milestones and any unforeseen challenges during development.

7. Budget:

The estimated budget for the project is 120,000. Any changes to the budget must be approved by the Product owner/project sponsor.

8. Risks:

- **Technical Risks:** Compatibility issues with existing systems.
- **User Adoption:** Resistance to providing feedback or using the new system.

9. Quality Assurance:

Regular testing and quality assurance measures will be implemented throughout the development process to ensure the reliability and effectiveness of the Continuous Feedback Application.

10. Approval:

This project charter is to be reviewed and approved by Product Owner before the commencement of the project.

Product Owner: @Areeba Ilyas **Date:** 30-10-2023

11. Project Sign-off:

Upon successful completion of the project, a sign-off will be obtained from the product owner/ Project sponsor indicating their satisfaction with the delivered Continuous Feedback Application.

Project Plan

Project Title: NrollXpert: Simple Application, Seamless Enrolment

Project Start Date: 27-10-2023

Project End Date: 12-01-2024

1. Project Planning

• Phase 1: Pre-Planning

- Define specific goals and objectives for the continuous feedback system.
- Formation of teams and Identify their roles.
- Complete Research Analysis & Team.
- Create User stories

• Phase 2: Sprints Planning

- Determine the data points to be collected.
- Gathered all requirements.
- Discuss System Design.
- **Product Backlog:**
 - Create a backlog of all features and functionalities needed.
 - Prioritize the backlog based on business value.
- **Sprint Planning:**
 - Select user stories from the backlog for the first sprint.
 - Break down user stories into tasks.

• Phase 3: Sprints Development

- **Sprint Execution (2 weeks each):**
 - Daily Stand-up Meetings: Short daily meetings to discuss progress and obstacles.
 - Develop Features: Design, code, test, and integrate features.
 - Test and QA: Regularly test the developed features.
- **Sprint Review:**
 - Demonstrate the completed features to stakeholders.

- Collect feedback for continuous improvement.
- **Sprint Retrospective:**
 - Reflect on the sprint, identify what went well and what could be improved.
 - Adjust the process accordingly.
- **Phase 4: Documentation & Deployment**
 - Deploy the seamless enrollment application.
 - Monitor initial feedback and address any emerging issues.

2. Resources:

- **IT Team:** Developers and Testers
- **End-users and Administrators:** FH Dortmund Students & Faculty

3. Budget:

The estimated budget for the project is 120,000 Euros. This includes development costs, training materials, and any unforeseen expenses. Budget adjustments will be communicated and approved by the project sponsor. Each employee will have 3000 Euro salary per month average. So if 10 Employee will work then total will be 90, 000 euro and 10,000 will be the extra cost.

4. Risks:

- **Technical Risks:** Compatibility issues with existing systems.
- **User Adoption:** Resistance to providing feedback or using the new system.

5. Communication Plan:

Regular communication updates will be provided to teams and stakeholders throughout the project. Meetings and progress reports will ensure transparency and alignment with project goals.

6. Approval:

This project plan is to be reviewed and approved by Product Owner before the commencement of the project.

Product Owner: Areeba Ilyas

7. Project Sign-off:

Upon successful implementation and integration of the continuous feedback mechanism, a sign-off will be obtained from the project sponsor indicating their satisfaction with the

delivered system.

Product Backlog

Sprint ID	Backlog Item ID	StoryPoints	Story	Assigned to	Status	Completed on
1	1	5	Home page: As a Prospective Applicant, I Want an Informative and Engaging Home Screen to get information about the available programs	Muhammad Tallal Bin Shahid	Done	11/30/2023
1	2	3	Program Details: As a Prospective Applicant, I Want a	Muhammad Tallal Bin Shahid	Done	11/30/2023

			Detailed Program Overview to Inform my Enrollment Decision			
1	3	5	Ask for authentication: As a Prospective Applicant, When I click on apply, if I'm not logged in I should be moved to a page that will ask me to login or create an account	Muhammad Tallal Bin Shahid	Done	12/1/2023

1	4	5	Login page: As a Prospective Applicant, I Want a Secure and Intuitive Login Screen to Access the Application Process	Ahmed Hobeishy	Done	12/1/2023
1	5	3	Chat system: As an applicant, I Want Quick Access to Support Chats for Different Programs	Silpa Prasad Sivaprasad	Done	12/2/2023
1	6	5	Application form: As an	Ahmed Hobeishy	Done	12/3/2023

			Applicant, I am Required to Provide Essential Personal Information for the University Application			
2	7	2	Create-account page: As a Prospective Applicant, I Want a Streamlined Account Creation Process to Begin the Program Application	Ahmed Hobeishy	Done	12/10/2023

2	8	2	Chat system: As an applicant, I Want a Centralized Chat Window to Manage Support Conversations for Different Programs	Silpa Prasad Sivaprasad	Done	12/12/2023
2	9	5	Guidelines Page: As an applicant navigating through the enrollment app, I want a comprehensive Guidelines page	Farhana	Done	12/14/2023

			that explains the entire application form flow.			
2	10	5	FAQs Page: As an applicant, I want a dedicated Frequently Asked Questions (FAQs) page that addresses commonly asked questions	Farhana	Done	12/16/2023
2	11	5	Application form: As an Applicant, I am Require	Ahmed Hobeishy	Done	12/17/2023

			d to Provide Essential Personal Information for the University Application			
2	12	8	Application form: As an Applicant, I Want to Upload Required Documents for the Precheck Process	Ahmed Hobeishy	Done	12/17/2023
2	13	8	Application form: As an Applicant, I Want to View the Status	Ahmed Hobeishy	Done	12/18/2023

			of My Applicati on After Submitti ng Docume nts for Pre- Check			
3	14	2	Chat system: As an Applican t, I Want to Access and Interact with Program - Specific Chat Threads	Silpa Prasad Sivapras ad	Done	12/25/2 023
3	15	13	Applican t form: As an Approve d Applican t, I Want to Submit All Require	Ahmed Hobeish y	Done	12/27/20 23

			d Informat ion and Docume nts for the Specific Program			
3	16	5	Applicati on form: As an Applican t, I Want to View the Status of My Applicati on After Submitti ng All Program Require ments	Ahmed Hobeish y	Done	12/28/2 023
3	17	5	Applicati on form: As an Applican t, I Want a Stepper to Track the Progres s of My	Ahmed Hobeish y	Done	12/28/2 023

			Applicati on Stages			
3	18	5	Applicati on dashboa rd: As an Applican t, I Want a Dashbo ard to Monitor the Status and Progres s of All My Applicati ons	Muham mad Tallal Bin Shahid	Done	12/30/2 023

Milestone Plan

Approver	@Areeba Ilyas
Contributors	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath @Farhana Binta Shaheed)
Objective	To create a user-friendly experience for applicants, make it easier for university staff to manage all applications and digitize the Enrollment process
Due date	12 January, 2024
Key outcomes	Enhanced User Experience Improved Communication Centralized Platform Data Accuracy and Security Analytics and Reporting Scalability and Flexibility Enrollment Rate and Stakeholder Satisfaction Cost-Efficiency
Status	NOT STARTED / IN PROGRESS / DONE

🧐 Problem Statement


“Current enrollment processes lack efficiency, accessibility, and user-friendliness, leading to a myriad of challenges for both applicants and administrators. The absence of a centralized and intuitive application platform results in time-consuming manual data entry, inconsistent user experiences, and limited accessibility for a diverse applicant pool. This fragmented system contributes to increased administrative workload, potential errors in data management, and a suboptimal enrollment rate. Addressing these issues through a comprehensive, streamlined, and user-centric application and enrollment app is crucial to enhance accessibility, reduce administrative burden, ensure data accuracy, and ultimately elevate the enrollment experience for all stakeholders involved.”

🎯 Scope

Must have:	1. User Authentication • Secure login for applicants and university staff. 2. Profiles for applicants and staff. 3. Dashboard • Show an overview of the application process and the status of the application. 4. Step-by-step guidance through the enrollment process.
-------------------	--

	• Checklist for required documents. • Secure file upload for required documents.
	5. Support and Guidance • FAQs and resources for common queries.
Nice to have:	• In-app messaging for communication between applicants and university staff. • Automated notifications for important updates. • Push notifications for updates and reminders.
Not in scope:	• Long-term support and maintenance strategies beyond the initial development phase • Fundamental changes to the organization's IT infrastructure that extend beyond the immediate needs of the application and enrollment process • Development of training programs for to the application and enrollment processes.

Timeline

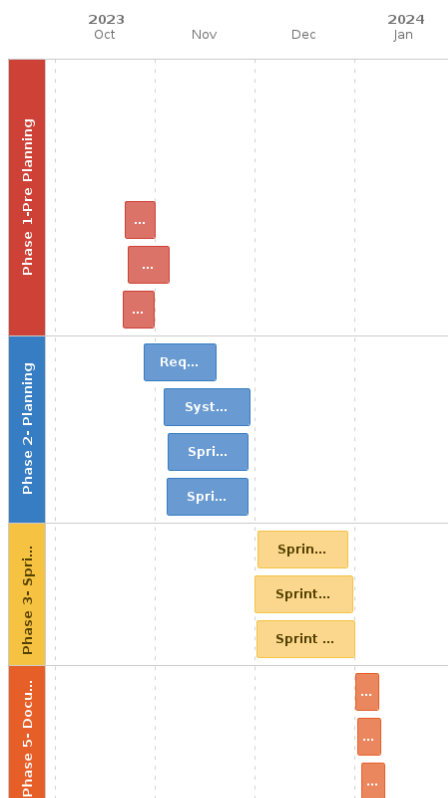


Milestones and deadlines

Milestone	Owner	Deadline	Status
• Define Project Scope, Identify Stakeholders, Set Project Goals and Objectives	@Ahmed Hobeishy @LAKSHA Y SAINI @Areeba Ilyas	30 October, 2023	DONE
• Role Definition	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath @Farhana Binta Shaheed)	3 November, 2023	DONE
• Conduct Kickoff Meeting	@Areeba Ilyas @Snigdha Nath	3 November, 2023	DONE
• Define User Stories Refinement	@Snigdha Nath @Ahmed Hobeishy	20 November, 2023	DONE
• Prioritize User Stories	@Snigdha Nath @Ahmed Hobeishy	20 November, 2023	DONE
• UI/UX Design	@Muham mad Tallal Bin Shahid @A hmed Hobeishy @Farhana Binta Shaheed @Silpa Prasad Sivaprasad @Mustafa Ali (BJ)	30 November, 2023	DONE

• Do User Authentication, Profile Creation, Basic Dashboard	@Mustafa Ali (BJ) @Ahmed Hobeishy @Farhana Binta Shaheed @Silpa Prasad Sivaprasad @Muham mad Tallal Bin Shahid	5 December, 2023	DONE
• Add Guidance and Checklist, File Upload, FAQs	@Mustafa Ali (BJ) @Ahmed Hobeishy @Silpa Prasad Sivaprasad @Farhana Binta Shaheed @Muham mad Tallal Bin Shahid	22 December, 2023	DONE
• Testing	@Anjali Khanduri @Nitika Deswal	28 December, 2023	DONE
• User Manuals and Technical Documentation	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri @LAKSHAY SAINI @Muhammad Tallal Bin Shahid @Mustafa Ali (BJ) @Nitika Deswal @Silpa Prasad Sivaprasad @Snigdha Nath @Farhana Binta Shaheed)	5 January, 2024	DONE
• Ready for launch/deploy	Team C (@Areeba Ilyas @Ahmed Hobeishy @Anjali Khanduri	8 January, 2024	DONE

	@Farhana Binta Shaheed	
	@LAKSHAY	
	SAINI	
	@Muhammad	
	Tallal Bin	
	Shahid	
	@Mustafa Ali	
	(BJ) @Nitika	
	Deswal @Silpa	
	Prasad	
	Sivaprasad	
	@Snigdha	
	Nath)	



Client Communication plan

1. Initial Discovery Meeting:

- **Understand Project Goals:** Gather detailed information about the app's purpose, target audience, and desired outcomes.
- **Define Scope:** Discuss features, functionalities, and specific requirements for student application and enrollment processes.

2. Regular Progress Updates:

- **Scheduled Check-ins:** Set up regular meetings (weekly or bi-weekly) to provide progress reports and ensure alignment with client expectations.
- **Demo Sessions:** Conduct demonstrations of app features as they are developed to gather feedback early in the process.

3. Clear Documentation:

- **Project Plan:** Present a detailed project plan outlining milestones, timelines, and deliverables related to application and enrollment functionalities.
- **Feature Specifications:** Document specific requirements for student application, enrollment forms, document submissions, etc.

4. Transparency in Development:

- **Version Releases:** Share beta versions or prototypes for the client to test functionalities related to student applications and enrollment.
- **Continuous Integration:** Show ongoing integration of features related to student enrollment within the app development process.

5. Accessibility and Support:

- **Accessible Communication Channels:** Offer multiple communication channels (email, project management tools, scheduled calls) for queries and discussions.
- **Dedicated Support:** Provide a clear point of contact for any issues related to student enrollment functionalities.

6. Feedback and Iteration:

- **Feedback Sessions:** Encourage feedback at various stages of development to refine the application and enrollment processes.
- **Iterative Approach:** Implement changes based on feedback received, ensuring the app aligns with the client's vision.

7. Training and Documentation for Client's Team:

- **Training Sessions:** Conduct sessions to train the client's team on using and managing student application and enrollment features.
- **Comprehensive Documentation:** Provide detailed guides/manuals for the app's enrollment functionalities.

8. Security and Compliance:

- **Security Measures:** Discuss and implement necessary security protocols for handling student data and enrollment processes.
- **Compliance Assurance:** Ensure the app complies with relevant regulations (e.g., GDPR, FERPA) concerning student information and privacy.

9. Post-Launch Support:

- **Post-Deployment Review:** Hold a meeting after the app launch to address any immediate issues and plan for ongoing support.
- **Ongoing Maintenance:** Offer maintenance services and support for any post-launch issues related to enrollment functionalities.

SharePoint Site for the Documentation

 <https://fhdoprod.sharepoint.com/:u:/r/sites/Stud-NrollXpert/SitePages/CollabHome.aspx?csf=1&web=1&e=XFz2AD> Connect your OneDrive account

Risk Register :

Risk ID	Risk Description	Probability	Impact
R1	Absence of team members	Medium	High
R2	Unable to complete the assigned task on Project Timeline	High	High
R3	Budget Cut	Low	High
R4	Budget cut in case of emergencies	Medium	Medium
R5	Ineffective Planning & organization	High	High
R6	Not enough time allocation for the tasks	High	High
R7	Technical Failures	Medium	High
R8	Wrong entity Permission	Medium	High
R9	False Navigation	Low	Medium

Test Strategy and Summary

Test Plan

Document Name	Test Strategy Document
Document Version	1.2
Author	@Nitika Deswal @Anjali Khanduri
Creation Date	15/11/2023
Approved By	@Areeba Ilyas
Approval Date	16/11/2023

Change History:

Doc Version	Author	Date	Description/Change
1.1	@Nitika Deswal @Anjali Khanduri	10/11/2023	2.3 Test Approach: tool updation 2.7 Test Deliverables updated

Testing Team:

Name		Role
Deswal, Nitika	@Nitika Deswal	Tester
Khanduri, Anjali	@Anjali Khanduri	Tester

1. Test Plan and Scheduling

Phase	Sprint	Milestone	Original Baseline	Rebase Plan	Actual	Status
Planning		Requirement Specification	04.11.2023		04.11.2023	DONE
		Test Strategy Preparation	10.11.2023		10.11.2023	DONE
		Test Strategy Review	15.11.2023	16.11.2023	17.11.2023	DONE
Design And Build	1	Test Script Construction	20.11.2023		20.11.2023	DONE
		Test Execution	23.11.2023	25.11.2023	26.11.2023	DONE
		Test Summary Report	04.12.2023		04.12.2023	DONE
		Risk Reporting	04.12.2023		04.12.2023	DONE
	2	Test Script Construction	05.12.2023		05.12.2023	DONE
		Test Execution	10.12.2023	11.12.2023	13.12.2023	DONE
		Test Summary Report	18.12.2023		18.12.2023	DONE
		Risk Reporting	18.12.2023		18.12.2023	DONE

	3	Test Script Construction	19.12.2023		19.12.2023	DONE
		Test Execution	22.12.2023	26.12.2023	26.12.2023	DONE
		Test Summary Report	01.01.2024		01.01.2024	DONE
		Risk Reporting	01.01.2024		01.01.2024	DONE
	4	Test Script Construction	02.01.2024		NA	
		Test Execution	05.01.2024	02.01.2024	02.01.2024	DONE
		Test Summary Report	11.01.2024	05.01.2024	05.01.2024	DONE
		Risk Reporting	11.01.2024	05.01.2024	05.01.2024	DONE
Test Closure		Test Summary Report and Sign-Off	12.01.2024	10.01.2024	11.01.2024	DONE

2. Test Scope

2.1 Purpose

This test plan outlines the strategic framework governing the comprehensive testing of the 'NrollXpert' application. It encompasses:

- **Test Strategy:** Detailing the foundational principles guiding the tests, including test objectives, and underlying assumptions. It defines the criteria for test setup, encompassing test scope, scope of testing, Level of Testing.
- **Execution Strategy:** Articulating the methodology for conducting the tests, including Acceptance Criteria, Test Deliverables.
- **Defect Management:** Articulating the methodology for managing and reporting the defects, including Defect Tracking, Defect Reporting and Test Metrics.

2.2 Project Scope

This project aims to develop an application outline on Figma. The application serves as a comprehensive academic and resource management platform within the university ecosystem. The application will focus on delivering essential features to facilitate academic operations and student engagement. The key functionalities include:

2.2.1 Exam Schedules and Policy:

- Displaying and managing exam schedules for different courses, semesters, and examination policies.
- Providing clear guidelines and regulations concerning exams and assessment procedures.

2.2.2 Financial Aid:

- Managing information related to financial aid, including application deadlines, required documentation, and submission processes.
- Facilitating the submission and tracking of necessary documentation for financial aid applications.

2.2.3 Course Registration:

- Enabling students to browse available courses, view timelines, pre-requisites, and waitlist information.
- Allowing registration for courses within defined timelines and providing waitlist management features.

2.2.4 Managing Academic Record:

- Providing access to academic records such as transcripts, grade reports, and GPA tracking.
- Offering tools for students to monitor and analyze their academic performance.

2.2.5 Campus Resources:

- Granting access to campus resources such as library facilities, study spaces, and other campus amenities.
- Providing information about campus facilities and their availability.

2.3 Audience

- Enrolled Students
- Applicants
- Faculty

3. Testing Objective

3.1 Test Objectives

The test objective is to ensure the NrollXpert functions in line with specifications. The test will execute and validate scripts, addressing defects within the entrance criteria. The test outcomes comprise:

- A refined software framework prepared for development.
- A collection of robust test scripts suitable for Functional and UAT test cycles, ensuring stability and reusability.

3.2 Test Assumptions

Assumptions for the test plan of the software designed in Figma, considering its non-functional state:

S.No.	Test Assumptions	Details
1	Design-Functionality Alignment	Figma designs accurately reflect intended functionalities outlined in requirements or specifications.
2	Interactivity Representation	Non-functional Figma designs effectively convey interactive elements and user flows for the final application.
3	Consistency in Design Elements	Design elements, layouts, and visual representations within Figma remain consistent and align with the overall design language.
4	Accessibility Consideration	Basic accessibility standards are reflected in Figma designs, although actual testing requires a functional application.

5	Data Representation Fidelity	Data presented in Figma designs mirrors expected real data, facilitating an accurate representation of content and functionality.
6	Collaborative Understanding	Shared understanding among stakeholders, designers, and testing teams regarding fidelity and interpretation of Figma designs.
8	Technical Limitations Disclosure	Acknowledgment and communication of any technical limitations within Figma that might restrict or impact accurate representation of intended functionalities and interactions.

These assumptions aim to ensure that despite the non-functional state of the software in Figma, there's a comprehensive understanding of the design's alignment with intended functionalities and interactions, fostering effective testing preparations.

4. Done (DoD)

The testing phase is considered 'Done' when it successfully meets the predetermined acceptance criteria. This includes thorough validation against functional requirements, execution of relevant test cases, documentation completion, and alignment with the overall project standards. Bugs identified during testing are expected to be closed. If any bugs remain open, the Product Owner collaborates to address and resolve them, ensuring a high-quality deliverable.

5. Testing Strategy

5.1. Test Approach

The testing strategy will involve manual validation to ensure that the screens align with the user's expectations and specified requirements. Trello is the tool used for Test Management. All testing artifacts, such as test cases and test results, are updated in Trello.

5.2. Scope of Testing

The scope of testing will focus exclusively on the validation of Figma screens to ensure they meet user expectations and align with specified requirements. Manual testing will be employed to verify the fidelity and accuracy of these screens.

The following types of testing are out of scope for the evaluation of Figma screens:

- Unit testing
- Functional testing
- Regression testing
- Sanity testing
- User Acceptance Testing (UAT)

5.3. Levels of Testing

The levels of testing delineate the stages or levels at which testing will be conducted to ensure comprehensive coverage. It includes:

Testing Category	Aspect	Objective
Visual Consistency and Accuracy	Layout and Alignment	Check for consistent layout and alignment of elements as per design specifications.
	Color and Typography	Verify that colors and typography are consistent and match the design guidelines.

	Icon and Image Resolution	Ensure icons and images display at the intended resolution and quality.
Functional Validation	Interactive Elements	Test buttons, links, dropdowns, etc., for responsiveness and accuracy.
	Navigation	Verify navigation paths within screens and between different sections.
	Form Submissions	Check input fields, form submissions, and error handling.
User Experience (UX)	Usability Testing	Evaluate ease of use, intuitiveness, and user-friendliness of the screens.
	Clarity and Readability	Ensure text and content are clear, readable, and appropriately sized.
	Consistency in Design Elements	Validate consistency in design patterns and elements across screens.
Accessibility and Responsiveness	Responsive Design	Test screen responsiveness across various devices and screen sizes.

	Basic Accessibility	Check contrast, readability, and navigation for basic accessibility standards.
User Flow Testing	End-to-End Scenario Testing	Test user flows through various scenarios to ensure smooth navigation and interactions.

These testing aim to validate different aspects of the Figma screens, ensuring their accuracy, functionality, usability, accessibility, and overall alignment with user expectations and design guidelines.

5.4. Test Acceptance Criteria

1. Functional Specification and Use Case documents should be approved and accessible before initiating the Test Design phase.
2. Development should be finalized and successfully pass unit testing.
3. The Figma test environment must be configured and in a functional state for use.

5.5. Test Deliverables:

S.No.	Deliverable Name	Author	Reviewer
1	Test Plan	Test Team	Product Owner/Requirements Team
2	Functional Test Cases	Test Team	Requirement's Team Sign off
3	Logging Defects in Trello	Test Team	Testing Team/Dev team
4	Daily/weekly status report	Test Team	Test team

5	Test Closure report	Test team	Product Owner
---	------------------------	-----------	---------------

6. Test Execution Strategy

6.1. Resource Requirement

S.No.	Resource Category	Description	Reviewer
1	Testers	A team of skilled manual testers proficient in visual validation, functional/non-functional testing, and usability testing. - Familiarity with Trello for defect tracking and reporting.	@Anjali Khanduri @Nitika Deswal
2	Development Team	Collaborates with testers to address and resolve defects in the Figma designs.	@Ahmed Hobeishy @Muhammad Tallal Bin Shahid @Silpa Prasad Sivaprasad
3	Figma Environment	Access to the Figma platform for all team members to review and validate designs.	
4	Trello	A shared Trello board for the test team to log defects, track progress, and report testing status.	

5	Documentation Expert	Ensures proper documentation of the test plan, test cases, and test closure report.	@Anjali Khanduri @Nitika Deswal
---	----------------------	---	------------------------------------

6.2. Risk Analysis:

S.No.	Resource Category	Probability	Impact	Mitigation
1	Design-Functionality Misalignment	Medium	High	Regular communication between the design and development teams to address any discrepancies.
2	Technical Limitations in Figma	Low	Moderate	Regular updates from the design team regarding any technical limitations, allowing adjustments in testing expectations.
3	Incomplete or Unclear Requirements	Medium	High	Frequent collaboration between testing and requirements teams to ensure clarity and completeness.
4	Unexpected Changes in Design Elements	Low	Moderate	Continuous communication channels to promptly address and adapt to design changes.

5	Unavailability of Figma Test Environment	Low	High	Regular checks on Figma environment availability, with a backup plan for delays.
6	Defect Resolution Delays	Medium	Moderate	Efficient communication channels between testing and development teams to prioritize and expedite defect resolutions.

Contingency Plan:

S.No.	Contingency Plan	What We'll Do if Things Go Wrong
1	Alternate Test Environment	In case of Figma unavailability, consider using alternative design review tools or staging environments for testing.
2	Rapid Communication Channels	Establish rapid communication channels to address unexpected changes or urgent issues, ensuring quick decision-making.
3	Parallel Testing Efforts	Have backup testers available to handle increased workload or urgent testing requirements.

6.3. Test Metrics

In Trello, the test metrics section categorizes defects discovered during testing based on High, Medium, and Low priority classifications.

Severity	Impact
----------	--------

1 High Priority	A High Priority bug has a significant impact, potentially causing a severe disruption in system functionality or compromising critical features.
2 Medium Priority	A Medium Priority bug has a moderate impact, leading to a degradation in system quality. While it may affect functionality, there is often an intelligent workaround or partial functionality available.
3 Low Priority	A Low Priority bug has minimal impact on product use, often associated with insufficient or unclear error messages that have negligible effects on overall functionality.

This system of prioritization within Trello ensures a focused and structured approach to managing and resolving identified issues during the testing process.

6.4. Validation and Defect Management

- Testers are anticipated to execute all scripts within each sprint. However, they are empowered to conduct additional testing if they detect potential gaps in the existing scripts.
- Defects will be logged and tracked using Trello. The technical team will gather daily information from Trello, and if necessary, request further details during team meetings or by adding comments to the bug. Subsequently, the technical team will proceed with fixes as needed.

6.5. Defect Tracking and Reporting

- Leveraging Trello as our designated platform for defect reporting and tracking in the testing process.
- Upon identification, defects will be logged and documented in Trello, with swift assignment to the development team for resolution.
- Post-fix implementation, a retesting phase will validate the efficacy of resolutions, ensuring successful defect management within our Trello-based testing framework.

Test Summary Report

This document serves as a repository for organizing and documenting essential information related to the software development lifecycle.

It systematically maintains records including Sprint details, the total number of identified bugs, distribution of bugs based on priority levels (High, Medium, Low), current status, an overview of open bugs, testing responsibility allocated to specific individuals or teams, and assignment details for bug resolution.

This structured approach ensures effective tracking, communication, and resolution of software defects throughout the development process.

1. Test Summary Report Sprint 1

Bug Details

1	Sprint	1	
2	Number of Bugs	6	
3	Number of bugs with High Priority	4	
4	Number of bugs with Medium Priority	2	
5	Number of bugs with Low Priority	0	
6	Open Bugs	0	
7	Closed Bugs	6	
8	Tested By	@Anjali Khanduri @Nitika Deswal	
9	Assigned To	@Ahmed Hobeishy @Silpa Prasad Sivaprasad @Muhammad Tallal Bin Shahid	
10	Risk	N/A	

2. Test Summary Report Sprint 2

Bug Details

1	Sprint	2	
2	Number of Bugs	4	
3	Number of bugs with High Priority	3	
4	Number of bugs with Medium Priority	0	
5	Number of bugs with Low Priority	1	
6	Open Bugs	0	
7	Closed Bugs	4	
8	Tested By	@Anjali Khanduri @Nitika Deswal	
9	Assigned To	@Ahmed Hobeishy , @Silpa Prasad Sivaprasad @Muhammad Tallal Bin Shahid	
10	Risk	N/A	

3. Test Summary Report Sprint 3

Bug Details

1	Sprint	3	
2	Number of Bugs	3	
3	Number of bugs with High Priority	1	
4	Number of bugs with Medium Priority	1	
5	Number of bugs with Low Priority	1	
6	Open Bugs	2	
7	Closed Bugs	1	
8	Tested By	@Anjali Khanduri @Nitika Deswal	
9	Assigned To	@Ahmed Hobeishy @Silpa Prasad Sivaprasad @Muhammad Tallal Bin Shahid	
10	Risk	N/A	

4. Test Summary Report Sprint 4

Bug Details

1	Sprint	4	
2	Number of Bugs	2	
3	Number of bugs with High Priority	0	
4	Number of bugs with Medium Priority	2	
5	Number of bugs with Low Priority	0	
6	Open Bugs	0	
7	Closed Bugs	2	
8	Tested By	@Anjali Khanduri @Nitika Deswal	
9	Assigned To	@Ahmed Hobeishy @Silpa Prasad Sivaprasad @Muhammad Tallal Bin Shahid	
10	Risk	N/A	

Testing Sign-Off

Sign-Off Report

Project Name: NrollXpert

Total Sprints: 4

Date: 10.01.2024

Summary of Testing Activities:

User Stories Tested:

User Story	Summary	Testing Status
User Story 1	Home page: As a Prospective Applicant, I Want an Informative and Engaging Home Screen to get information about the available programs	Passed
User Story 2	Program Details: As a Prospective Applicant, I Want a Detailed Program Overview to Inform my Enrollment Decision	Passed
User Story 3	Ask for authentication: As a Prospective Applicant, When I click on apply, if I'm not logged in I should be moved to a page that will ask me to login or create an account	Passed
User Story 4	Login page: As a Prospective Applicant, I Want a Secure and Intuitive Login Screen to Access the Application Process	Passed
User Story 5	Chat system: As an applicant, I Want Quick Access to Support Chats for Different Programs	Passed

User Story 6	Application form: As an Applicant, I am Required to Provide Essential Personal Information for the University Application	Passed
User Story 7	Create-account page: As a Prospective Applicant, I Want a Streamlined Account Creation Process to Begin the Program Application	Passed
User Story 8	Chat system: As an applicant, I Want a Centralized Chat Window to Manage Support Conversations for Different Programs	Passed
User Story 9	Guidelines Page: As an applicant navigating through the enrollment app, I want a comprehensive Guidelines page that explains the entire application form flow.	Passed
User Story 10	FAQs Page: As an applicant, I want a dedicated Frequently Asked Questions (FAQs) page that addresses commonly asked questions	Passed
User Story 11	Application form: As an Applicant, I Want to Upload Required Documents for the Precheck Process	Passed
User Story 12	Application form: As an Applicant, I Want to View the Status of My Application After Submitting Documents for Pre-Check	Passed
User Story 13	Chat system: As an Applicant, I Want to Access and Interact with Program-Specific Chat Threads	Passed
User Story 14	Applicant form: As an Approved Applicant, I Want to Submit All Required Information and Documents for the Specific Program	Passed

User Story 15	Application form: As an Applicant, I Want to View the Status of My Application After Submitting All Program Requirements	Passed
User Story 16	Application form: As an Applicant, I Want a Stepper to Track the Progress of My Application Stages	Passed
User Story 17	Application dashboard: As an Applicant, I Want a Dashboard to Monitor the Status and Progress of All My Applications	Passed

Bugs Reported:

Sprint	Total bugs	Open bugs	Closed bugs
1	6	0	6
2	4	0	4
3	3	0	1
4	2	0	2

Testing Sign-Off:

Tester Name: @Nitika Deswal @Anjali Khanduri

Date of Sign-Off: 10.01.2024

Test Environment: Figma

Additional Comments:

Testing was conducted to verify that Figma screens meet the acceptance criteria for the finalized requirements. Consequently, the Figma product is deemed complete from a testing perspective and is ready for use in development.

Approval:

Product Owner: @Areeba Ilyas

Date of Approval: 11.01.2024

Lesson Learned :

What went well	• Effective Collaboration • Timely Delivery • Adaptability and Flexibility • Encouraging Team Culture • Sprint Success
What could we Improve	Resource Optimization , Communication Gaps, stakeholder Involvement

Definition Of Done Checklist

User Story: Definition of Done Checklist	
☒	UX Design reviewed and accepted
☒	Completed unit testing
☒	Acceptance criteria met
☒	Functional tests passed
☒	Non-functional requirements met
☒	User stories approved by Product Owner
☒	Demo presentation and acceptance
☒	Prototype accepted
☒	Feature documentation done
☒	Signed off by Product Owner

Sprint: Definition of Done Checklist	
☒	Satisfied DoD for each user story in the sprint
☒	Compliance review is complete
☒	Configuration documented
☐	Performance testing is complete
☒	Security testing is complete
☒	Sprint marked as ready for deployment

Release: Definition of Done Checklist	
☒ Satisfied DoD for each sprint in the release	
☒ Production environment is ready	
☒ Rollback process is documented	
☒ Smoke testing scenarios are ready	
☒ Release communications are sent	
☒ Stakeholders signed off for the release	
